



450 - 1 Street SW  
Calgary, Alberta T2P 5H1

Tel: (403) 920-7425  
E-mail: [kenneth\\_pountney@tcenergy.com](mailto:kenneth_pountney@tcenergy.com)

April 20, 2026

Filed Electronically

Canada Energy Regulator  
Suite 210, 517 Tenth Avenue SW  
Calgary, Alberta T2R 0A8

**Attention: Ramona Sladic, Secretary of the Commission**

Dear Ramona Sladic:

**Re: NGTL GP Ltd. (NGTL GP), as general partner on behalf of  
NGTL Limited Partnership  
2025 Pipelines and Associated Facilities Decommissioning Program (Program or  
2025 Decommissioning Program)  
Order ZO-001-2006 (Order)  
Condition 4: Detailed Schedules  
File No.: 6503130**

In accordance with the condition of the Order,<sup>1</sup> NGTL GP submits the current decommissioning schedules which identifies major activities applicable to each site.

NGTL GP notes that the Order directs NGTL GP to notify the Canada Energy Regulator (CER) of any modifications to the schedules as they occur. Due to the nature of the work and availability of regional resources (specifically gas handling), changes to the schedule are expected to occur with limited notice.

As such, and consistent with its approach for schedule updates with previous Decommissioning Programs, NGTL GP proposes to provide the CER with quarterly (end of each quarter starting June 2026) schedule updates through the course of Decommissioning Activities.

NGTL GP confirms it will work with potentially affected stakeholders as schedule changes occur and as Decommissioning Activities progress.

For enquiries, please contact me at (403) 920-7425 or at [kenneth\\_pountney@tcenergy.com](mailto:kenneth_pountney@tcenergy.com).

Yours truly,  
**NGTL GP Ltd., as general partner on behalf of  
NGTL Limited Partnership**

*Original signed by*

Kenneth Pountney  
Regulatory Project Manager,  
Regulatory Facilities, Canadian Natural Gas Pipelines

Attachment

---


<sup>1</sup> Filing ID: C38689.

2025 Decommissioning - CER condition 4

Date Date: 09-Apr-26

Date Printed: 13-Apr-26

Activity ID	Activity Name	Original Duration	Start	Finish	2026												2027												2028		
					A	M	J	Jul	A	S	O	N	D	J	F	M	A	M	J	Jul	A	S	O	N	D	J	F	M			
<b>2025 Decommissioning Program - CER Condition 4</b>					373.0d												27-May-26												24-Aug-27		
<b>Rocky Mountain</b>					363.0d												07-Jun-26												24-Aug-27		
<b>North Lateral Extension (NPS 12 1969) Flat Lake Lateral Stage I Relocation</b>					26.0d												11-Apr-27												11-May-27		
A23700	Locate all underground facilities	2.0d	11-Apr-27	12-Apr-27																											
A23690	Mobilization	1.0d	13-Apr-27*	13-Apr-27																											
A23710	Access	2.0d	14-Apr-27	15-Apr-27																											
A23720	Daylighting of buried facilities	2.0d	15-Apr-27	16-Apr-27																											
A23730	Mechanical isolation (by cutting & capping or installation of blind flanges)	4.0d	20-Apr-27*	23-Apr-27																											
A23740	Pigging for cleaning / blind flange install after completed (for laterals only)	4.0d	28-Apr-27	01-May-27																											
A23750	Modify Cathodic Protection, where required	3.0d	02-May-27	04-May-27																											
A23760	Dispose of waste materials	2.0d	05-May-27	06-May-27																											
A23770	Backfill	2.0d	07-May-27	08-May-27																											
A23780	Recontour, Site seeding, where required	2.0d	09-May-27	10-May-27																											
A23790	Demobilization	1.0d	11-May-27	11-May-27																											
<b>Atlee Buffalo Lateral (NPS 6 1958)</b>					52.0d												28-Jun-26												30-Aug-26		
A23810	Locate all underground facilities	2.0d	28-Jun-26	29-Jun-26																											
A23800	Mobilization	1.0d	30-Jun-26*	30-Jun-26																											
A23820	Access	2.0d	01-Jul-26	02-Jul-26																											
A23830	Daylighting of buried facilities	6.0d	02-Jul-26	07-Jul-26																											
A23840	Mechanical isolation (by cutting & capping or installation of blind flanges)	3.0d	04-Aug-26*	06-Aug-26																											
A23850	Pigging for cleaning / blind flange install after completed (for laterals only)	4.0d	08-Aug-26	11-Aug-26																											
A23860	Modify Cathodic Protection, where required	4.0d	13-Aug-26	16-Aug-26																											
A23870	Dispose of waste materials	4.0d	18-Aug-26	21-Aug-26																											
A23880	Backfill	4.0d	22-Aug-26	25-Aug-26																											
A23890	Recontour, Site seeding, where required	4.0d	26-Aug-26	29-Aug-26																											
A23900	Demobilization	1.0d	30-Aug-26	30-Aug-26																											
<b>North Lateral Extension (NPS 16 1972) Stage 1 Brooks</b>					101.0d												07-Jun-26												06-Oct-26		
A25560	Locate all underground facilities	2.0d	07-Jun-26	08-Jun-26																											
A25570	Mobilization	1.0d	09-Jun-26*	09-Jun-26																											
A25580	Access	2.0d	10-Jun-26	11-Jun-26																											
A25590	Daylighting of buried facilities	2.0d	11-Jun-26	12-Jun-26																											
A25600	Mechanical isolation (by cutting & capping or installation of blind flanges)	7.0d	13-Jul-26*	19-Jul-26																											
A25610	Pigging for cleaning / blind flange install after completed (for laterals only)	10.0d	24-Jul-26	02-Aug-26																											
A25620	Modify Cathodic Protection, where required	10.0d	07-Aug-26	16-Aug-26																											

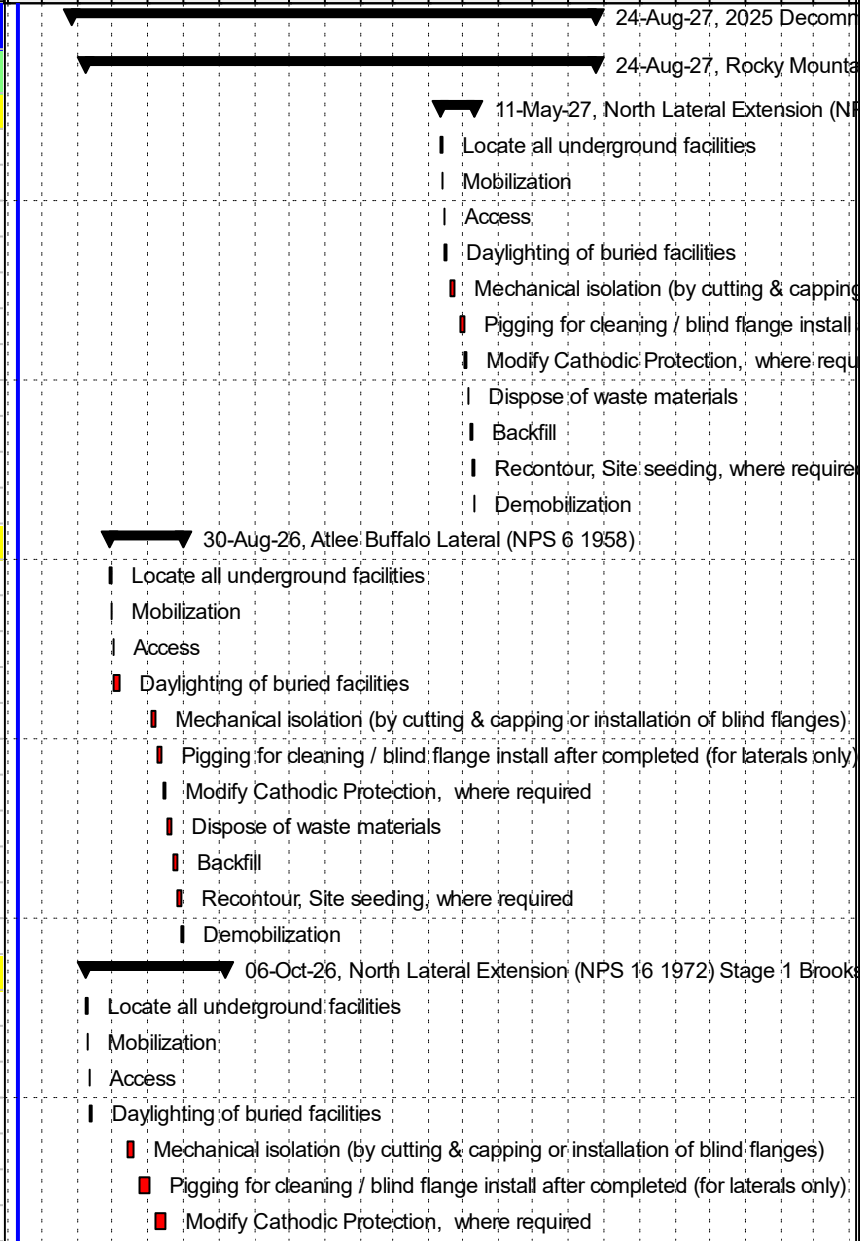

■ Actual Work   
 ■ Critical Remaining Work   
 ▼ Summary   
 ■ Remaining Work   
 ◆ Milestone









